



City of South Amboy

140 North Broadway • South Amboy, New Jersey 08879

Phone: (732) 727-4600

Fax: (732) 727-6139

Mark J. Rasimowicz, PE, PP, CME

City Engineer

Reply To:

481 Spotswood Englishtown Road

Monroe Township, NJ 08831

732-605-9440 / (fax) 732-605-9444

PERMIT APPLICATION FORM CURB/SIDEWALK CONSTRUCTION

Application Checklist:

(Failure to submit any of the items listed below will result in denial of permit)

- ___ 1. Application, completed in full and signed.
- ___ 2. Survey/sketch of all area to be disturbed. This must include dimensions of all work areas.
- ___ 3. Check for all calculated fees. (Check to be made payable to *'The City of South Amboy'*)

- All applications are to be submitted to the City Engineer via mail or hand delivery.
- Applications are processed within 5-7 business days of receipt.
- A letter of approval or denial will be sent via mail to the contact person identified on the permit.
- Construction cannot begin until the applicant has received an approval letter from the City Engineer and the Engineer has been notified of intended start date.

All applications are to be submitted to the City Engineer:

Center State Engineering
Mark J. Rasimowicz, PE, PP, CME
481 Spotswood Englishtown Road
Monroe Township, NJ 08831
Ph: (732) 605-9440

CITY OF SOUTH AMBOY
140 NORTH BROADWAY
SOUTH AMBOY, NJ 08879

PERMIT APPLICATION FORM CURB/SIDEWALK CONSTRUCTION

1. OWNER'S INFORMATION

NAME: _____
ADDRESS: _____
PHONE NO.: _____
EMAIL: _____

2. CONTRACTOR'S INFORMATION

NAME: _____
ADDRESS: _____
PHONE NO.: _____
EMAIL: _____

CONTACT PERSON: (circle one) OWNER or CONTRACTOR

3. LOCATION OF WORK

STREET ADDRESS: _____
TAX MAP BLOCK: _____ TAX MAP LOT: _____

4. TYPE OF PERMIT (CHECK ALL APPROPRIATE)

_____ Curb Construction/Replacement	_____ LF
_____ Sidewalk Construction/Replacement	_____ SF
_____ Driveway Apron Construction/Replacement	_____ SF

5. DESCRIPTION OF WORK

6. FEE

Curb: \$2.00 per each linear foot of curb
Sidewalk: \$0.50 per each square foot of sidewalk
Driveway Apron: \$0.50 per each square foot of sidewalk

Enclosed is the required fee of \$_____ (\$50.00 minimum)

7. CONDITIONS

- A. All sidewalks and curbs constructed, reconstructed, or repaired shall be in compliance with the current development regulations of the City of South Amboy.
- B. All sidewalks and curbs constructed, reconstructed, or repaired within the Special Design District of the City of South Amboy shall be in compliance with the established standards set forth in the Ordinance.
- C. All work performed shall be done in a good and workman like manner to the standards prescribed herein and to the reasonable satisfaction of the City Engineer.
- D. All damage to adjoining areas resulting from this construction shall be the responsibility of the owner and shall be repaired to the satisfaction of the City Engineer.
- E. No pavement should be disturbed as part of this construction.
- F. Only whole sections of curb shall be removed and replaced.
- G. It shall be the responsibility of the owner or his contractor to notify the City Engineer at least twenty-four (24) hours in advance of the following:
 - 1. Excavation and removal of existing curb and sidewalk.
 - 2. Setting of forms
 - 3. Placement of concrete.

OWNER'S NAME (Print)

OWNER'S SIGNATURE

DATE

CONTRACTOR'S NAME (Print)

CONTRACTOR'S SIGNATURE

DATE

APPLICATION NO.: _____


APPROVED: _____

DISAPPROVED: _____

ENGINEER


DATE

SKETCH OF PROPOSED WORK

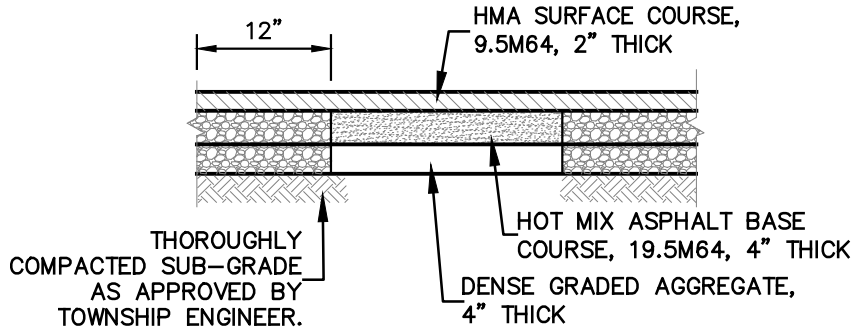

TYPICAL PAVEMENT REPAIR SECTION

NOT TO SCALE

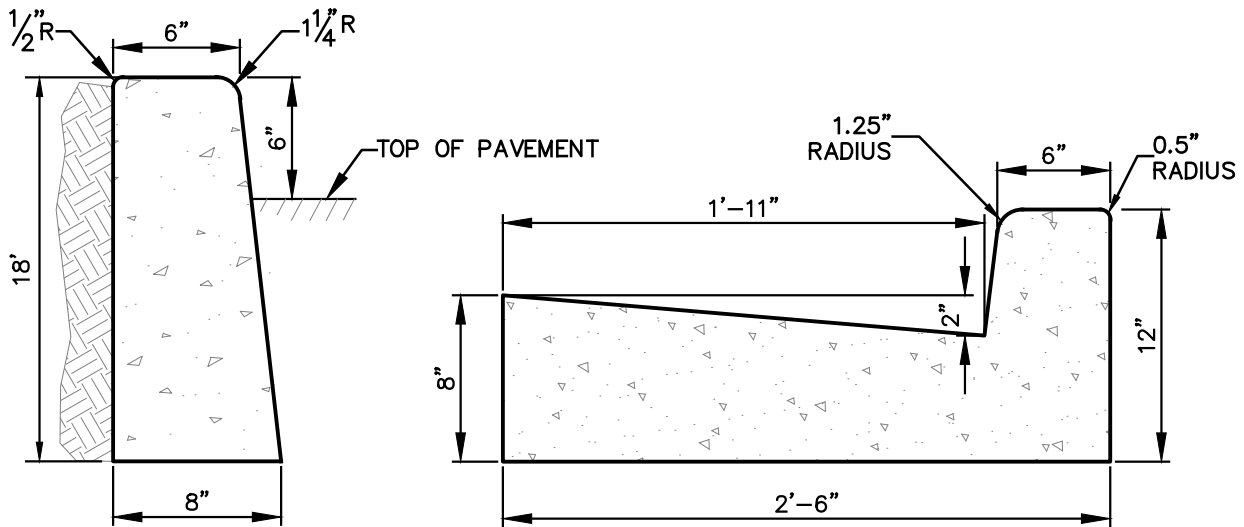

GENERAL NOTES:

1. ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE, AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY".
2. CONCRETE TO BE CLASS 'B' AIR-ENTRAINED.
3. TRANSVERSE JOINTS 1/2" WIDE SHALL BE INSTALLED IN THE CURB 20 FEET APART AND SHALL BE FILLED WITH PREFORMED, BITUMINOUS IMPREGNATED FIBER JOINT FILLER, COMPLYING WITH THE REQUIREMENTS OF AASHTO M-213, RECESSED 1/4" FROM THE FRONT FACE AND TOP OF THE CURB.
4. CONSTRUCTION JOINTS (FORMED) SHALL BE INSTALLED MIDWAY BETWEEN EXPANSION JOINTS.
5. CONCRETE SLUMP TO BE A MAXIMUM OF 3" OR AS DIRECTED BY THE TOWNSHIP ENGINEER.

CONCRETE CURB & GUTTER DETAIL

NOT TO SCALE

COPYRIGHT 2024, CENTER STATE ENGINEERING ASSOCIATES, INC. - ALL RIGHTS RESERVED. THE COPYING OR RE-USE OF THESE DOCUMENTS OR PORTIONS THEREOF, FOR OTHER THAN THE ORIGINAL PROJECT OR THE PURPOSE ORIGINALLY INTENDED, WITHOUT THE WRITTEN PERMISSION OF CENTER STATE ENGINEERING ASSOCIATES, INC., IS PROHIBITED.

CENTER STATE
ENGINEERING


481 Spotswood Englishtown Road, Monroe Township, New Jersey 08831

Phone: 732.605.9440

www.CenterStateEngineering.com

Fax: 732.605.9444

PROJECT:		ROAD OPENING PERMIT	
DRAWN BY:	CAL	LOCATION:	CITY OF SOUTH AMBOY, MIDDLESEX COUNTY, NEW JERSEY
DESIGNED BY:	CAL	LOT AND BLOCK:	
CHECKED BY:	MJR	TITLE:	DETAILS
APPROVED BY:	MJR	SCALE:	AS NOTED
PROJECT MANAGER:	PM	ISSUE DATE:	06/21/24
		PROJECT NO.:	
		SHEET NO.:	1 OF 3
		 MARK J. PASIMOWICZ, P.E. NEW JERSEY PROFESSIONAL ENGINEER LICENSE NO. 24GE04248700 NEW JERSEY CERTIFICATE OF AUTHORIZATION NO. 24GA28247000	

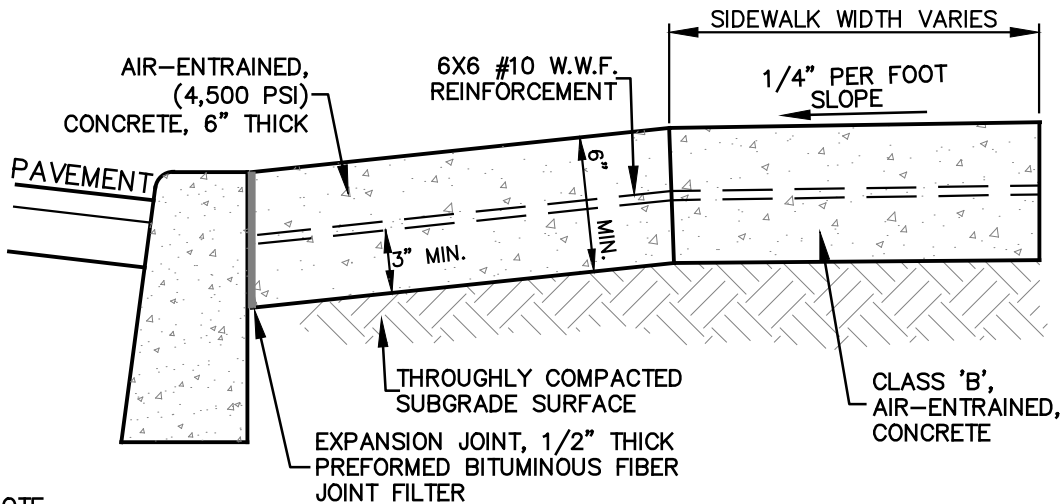


NOTE

1. ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE, AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY".
2. CONCRETE APRON SHALL BE EVENLY DIVIDED WITH EXPANSION JOINTS SUCH THAT NO PANEL EXCEEDS 20' IN ANY DIMENSION.
3. 6" THICK REINFORCED CONCRETE SHALL EXTEND A MINIMUM OF 3" BEYOND EDGE OF ALL DRIVEWAYS.
4. DIRECTION OF SLOPE AND GRADE TO BE AS SHOWN ON GRADING PLANS.

CONCRETE APRON WITH SIDEWALK

NOT TO SCALE

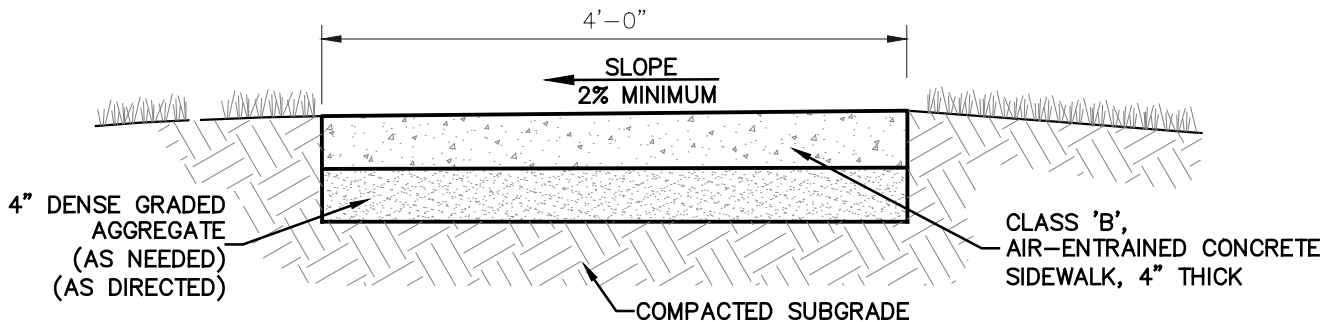

NOTE:

1. ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE, AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY".
2. SIDEWALK SHALL BE 4" THICK, AIR-ENTRAINED CONCRETE AT DRIVEWAYS. PROVIDE TOOLED JOINT EVERY 4' AND 1/2" PREMOLDED ASPHALT. IMPREGNATE EXPANSION JOINT EVERY 20'. (TYPICAL FOR MINOR STREET).

CONCRETE SIDEWALK DETAIL

NOT TO SCALE

COPYRIGHT 2024, CENTER STATE ENGINEERING ASSOCIATES, INC. - ALL RIGHTS RESERVED. THE COPYING OR RE-USE OF THESE DOCUMENTS OR PORTIONS THEREOF, FOR OTHER THAN THE ORIGINAL PROJECT OR THE PURPOSE ORIGINALLY INTENDED, WITHOUT THE WRITTEN PERMISSION OF CENTER STATE ENGINEERING ASSOCIATES, INC., IS PROHIBITED.



481 Spotswood Englishtown Road, Monroe Township, New Jersey 08831

Phone: 732.605.9440

www.CenterStateEngineering.com

Fax: 732.605.9444

PROJECT: ROAD OPENING PERMIT			
DRAWN BY: CAL	LOCATION: CITY OF SOUTH AMBOY, MIDDLESEX COUNTY, NEW JERSEY		
DESIGNED BY: CAL	LOT AND BLOCK: LOT:	BLOCK:	
CHECKED BY: MJR	TITLE: DETAILS		SCALE: AS NOTED
APPROVED BY: MJR			ISSUE DATE: 06/21/24
PROJECT MANAGER: PM			PROJECT NO:
 MARK J. PASIMOWICZ, P.E. NEW JERSEY PROFESSIONAL ENGINEER LICENSE NO. 24GE04248700 NEW JERSEY CERTIFICATE OF AUTHORIZATION NO. 24GA28247000			SHEET NO: 2 OF 3

