



City of South Amboy

Curb/Sidewalk Construction Permit

Application Checklist:

(Failure to submit any of the items listed below will result in denial of permit)

- ___ 1. Application, completed in full and signed.
 - ___ 2. Survey/sketch of all area to be disturbed. This must include dimensions of all work areas.
 - ___ 3. Check for all calculated fees. Check to be made payable to 'City of South Amboy'
- All applications are to be submitted to the City Engineer via mail or hand delivery.
 - Applications are processed within 5-7 business days of receipt.
 - A letter of approval or denial will be sent via mail.
 - Construction cannot begin until the applicant has received an approval letter from the City Engineer.

All applications are to be submitted to the City Engineer:

Feist Engineering, Inc.
Mark J. Rasimowicz, PE, PP, CME
481 Spotswood Englishtown Road
Monroe Township, NJ 08831
Ph: (732) 605-9440

CITY OF SOUTH AMBOY
140 NORTH BROADWAY
SOUTH AMBOY, NEW JERSEY 08879

PERMIT APPLICATION FORM
CURB/SIDEWALK CONSTRUCTION

1. OWNER(S) INFORMATION

Name: _____

Address: _____

Phone No: _____

2. CONTRACTOR(S) INFORMATION

Name: _____

Address: _____

Phone No: _____

3. LOCATION OF WORK

Street Address: _____

Tax Map Block: _____ Tax Map Lot _____

4. TYPE OF PERMIT (Check all appropriate)

_____ Curb Construction/Replacement _____ LF

_____ Sidewalk Construction/Replacement _____ SF

_____ Driveway Construction/Replacement _____ SF

5. DESCRIPTION OF WORK

6. FEE

Curb: \$1.00 per each linear foot of curb.
Sidewalk: \$0.25 per each square foot of sidewalk.
Driveway: \$0.25 per each square foot of driveway.

Enclosed is the required fee of \$ _____ (\$20.00 Minimum Fee)

7. CONDITIONS

- A. All sidewalks and curbs constructed, reconstructed or repaired shall be in compliance with the current development regulations of the City of South Amboy.
- B. All sidewalks and curbs constructed, reconstructed or repaired within the Special Design District of the City of South Amboy shall be in compliance with the established standards set forth in that Ordinance.
- C. All work performed shall be done in a good and workmanlike manner to the standards prescribed herein and to the reasonable satisfaction of the City Engineer.
- D. All damage to adjoining areas resulting from this construction shall be the responsibility of the owner and shall be repaired to the satisfaction of the City Engineer.
- E. No pavement should be disturbed as part of this construction.
- F. Only whole sections of curb shall be removed and replaced.
- G. It shall be the responsibility of the owner or his contractor to notify the City Engineer at least twenty-four (24) hours in advance of the following:
 - 1. Excavation and removal of existing curb and sidewalk.
 - 2. Setting of forms.
 - 3. Placement of concrete.

OWNER'S NAME (Print)

OWNER'S SIGNATURE

DATE

CONTRACTOR'S NAME (Print)

CONTRACTOR'S SIGNATURE

DATE

APPLICATION NO.: _____


APPROVED: _____


DISAPPROVED: _____

ENGINEER

DATE

SKETCH OF PROPOSED WORK



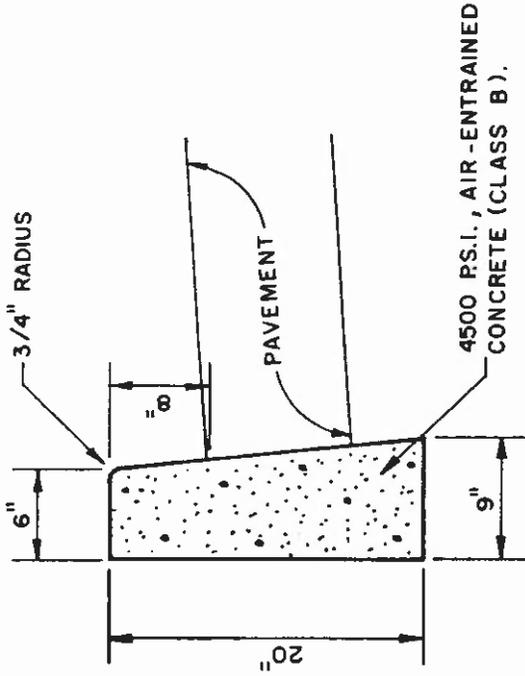


- NOTES:
1. MAXIMUM SLAB LENGTH TO BE 10'.
 2. PROVIDE 1/2" PREMOLDED ASPHALT IMPREGNATED EXPANSION JOINTS EVERY 20'.

CONCRETE CURB N.T.S.

NOTE: ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY."

CITY OF SOUTH AMBOY
STANDARD DETAIL




4" AIR-ENTRAINED CONCRETE SIDEWALK, 4000 P.S.I. (CLASS C).
 6" THICK AIR-ENTRAINED CONCRETE SIDEWALK AT DRIVEWAYS.
 PROVIDE TOOLED JOINT EVERY 4' AND 1/2" PREMOLDED
 ASPHALT IMPREGNATE EXPANSION JOINT EVERY 20'.
 (TYPICAL FOR MINOR STREET)

4" BANK RUN SAND, TYPE I (CLASS A).

SIDEWALK DETAIL N.T.S.

NOTE: ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY."

CITY OF SOUTH AMBOY
 STANDARD DETAIL

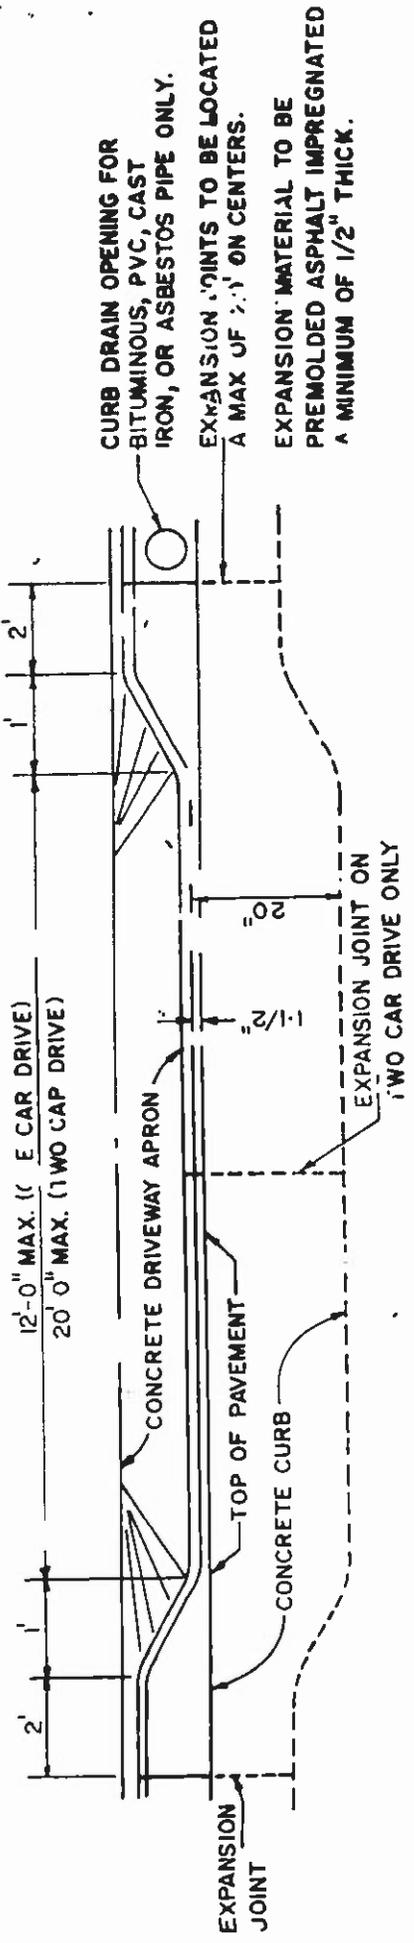


CURB DRAIN OPENING FOR BITUMINOUS, PVC, CAST IRON, OR ASBESTOS PIPE ONLY.

EXPANSION JOINTS TO BE LOCATED A MAX OF 20' ON CENTERS.

EXPANSION MATERIAL TO BE PREMOLED ASPHALT IMPREGNATED A MINIMUM OF 1/2" THICK.

ELEVATION

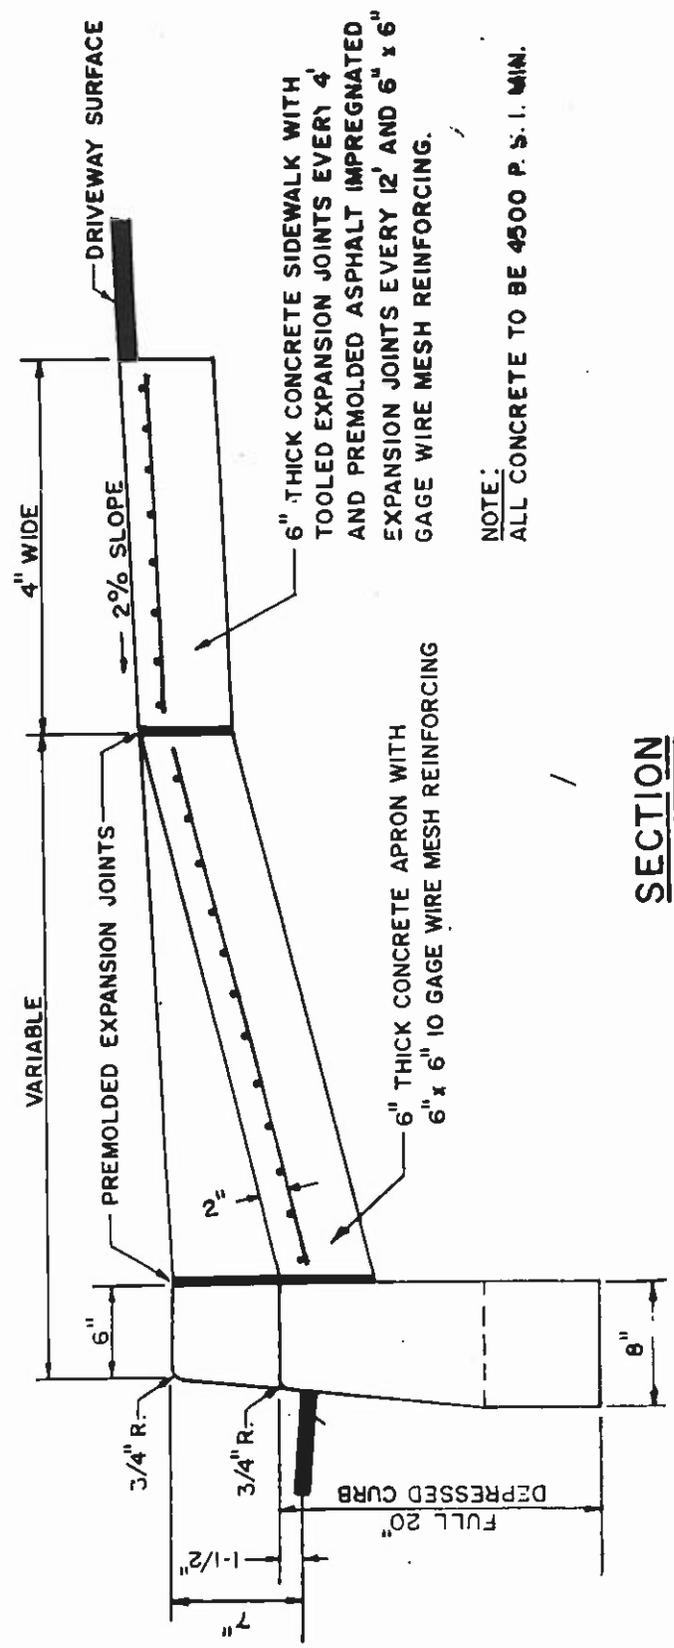

NOTE:
ALL CONCRETE TO BE 4500 P. S. I. MIN.

SECTION

DRIVEWAY APRON DETAIL N.T.S.

NOTE: ALL CONCRETE INSTALLED WITHIN SOUTH AMBOY'S SPECIAL DESIGN DISTRICT SHALL BE COLOR CONDITIONED WITH THE INTRODUCTION OF "CHROMIX" ADMIXTURE AS MANUFACTURED BY THE L. M. SCOFIELD COMPANY OR APPROVED EQUAL. THE COLOR SHALL BE "FRENCH GRAY."

CITY OF SOUTH AMBOY
STANDARD DETAIL
